


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Dec																											
							Qtr 1, 2022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	Qtr 2, 2023	Qtr 3, 2023																					
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug								
1		The Definitive Windows 11 Enterprise Migration Project Plan by Juriba	429 days	Mon 03/01/2	Thu 24/08/23																													
2		Plan & Mobilisation Phase	39 days	Mon 03/01/2	Thu 24/02/22																													
3		Proposal	15 days	Mon 03/01/2	Fri 21/01/22																													
4		Identify Business Need For Project	5 days	Mon 03/01/2	Fri 07/01/22																													
5		Document business benefits of Win 11 migration project	5 days	Mon 03/01/2	Fri 07/01/22																													
6		Identify Key Project Stakeholders	1 day	Mon 10/01/2	Mon 10/01/2																													
7		Identify Business Sponsors	1 day	Mon 10/01/2	Mon 10/01/2	5																												
8		Identify IT Executive Sponsors	1 day	Mon 10/01/2	Mon 10/01/2	5																												
9		Create Business Case Document	9 days	Tue 11/01/22	Fri 21/01/22																													
10		Document Project Objectives	1 day	Tue 11/01/22	Tue 11/01/22	8																												
11		Document Project Acceptance Criteria	0.5 days	Wed 12/01/2	Wed 12/01/2	10																												
12		Document Project Scope Boundaries (in/out)	0.25 days	Wed 12/01/2	Wed 12/01/2	11																												
13		Document Project Requirements and Deliverables	0.5 days	Wed 12/01/2	Thu 13/01/22	12																												
14		Document Project Constraints	0.5 days	Thu 13/01/22	Thu 13/01/22	13																												
15		Document Project Assumptions and Dependencies	1 day	Thu 13/01/22	Fri 14/01/22	14																												
16		Document Initial Project Organisation	0.5 days	Fri 14/01/22	Mon 17/01/2	15																												
17		Document Initial Defined Issues and Risks	0.25 days	Mon 17/01/2	Mon 17/01/2	16																												
18		Document Key Schedule Milestones	0.25 days	Mon 17/01/2	Mon 17/01/2	17																												
19		Document Initial Work Breakdown Structure	1 day	Mon 17/01/2	Tue 18/01/22	18																												
20		Document Order of Magnitude Cost Estimate	1 day	Tue 18/01/22	Wed 19/01/2	19																												
21		Document Approval Requirements	0.25 days	Wed 19/01/2	Wed 19/01/2	20																												
22		Document Project Management Methodology	0.25 days	Thu 20/01/22	Thu 20/01/22	21																												
23		Document Project Management Information System	0.25 days	Thu 20/01/22	Thu 20/01/22	22																												
24		Document Operational Risk Requirements	1 day	Thu 20/01/22	Fri 21/01/22	23																												
25		Create & Present Initial Project Pitch To Stakeholders and Sponsors	0.5 days	Fri 21/01/22	Fri 21/01/22	24																												
26		MILESTONE: Business Case Document Approval	0 days	Fri 21/01/22	Fri 21/01/22	24																												
27		Build Project Management Repository & Documentation	18.5 days	Fri 21/01/22	Wed 16/02/2																													
28		Define project scope management plan (change management)	0.5 days	Fri 21/01/22	Fri 21/01/22	24																												
29		Define schedule management plan	0.5 days	Mon 24/01/2	Mon 24/01/2	28																												
30		Cost Management	1 day	Mon 24/01/2	Tue 25/01/22																													
31		Build cost tracking & control plan	1 day	Mon 24/01/2	Tue 25/01/22	29																												
32		Resource Management Plan	2.75 days	Tue 25/01/22	Fri 28/01/22																													
33		Document Resource Tracking Plan	0.75 days	Tue 25/01/22	Wed 26/01/2	31																												
34		Estimate Resource Roles and Requirements	1 day	Wed 26/01/2	Thu 27/01/22	33																												
35		Document Third Party Management Plan (if required)	1 day	Thu 27/01/22	Fri 28/01/22	34																												
36		RAIDs Management Plan	2.5 days	Fri 28/01/22	Tue 01/02/22																													
37		Build Risk Management Log	0.5 days	Fri 28/01/22	Fri 28/01/22	35																												
38		Build Assumptions Management Log	0.5 days	Fri 28/01/22	Mon 31/01/2	37																												
39		Build Issues Management Log	0.5 days	Mon 31/01/2	Mon 31/01/2	38																												
40		Build Dependencies Management Log	0.5 days	Mon 31/01/2	Tue 01/02/22	39																												
41		Build Operational Risk Plan	0.5 days	Tue 01/02/22	Tue 01/02/22	40																												
42		Operational Management Plan	4 days	Tue 01/02/22	Mon 07/02/2																													
43		Build procurement / contract management plan	0.5 days	Tue 01/02/22	Wed 02/02/2	41																												
44		Build quality management plan	0.5 days	Wed 02/02/2	Wed 02/02/2	43																												
45		Build configuration management plan	0.5 days	Wed 02/02/2	Thu 03/02/22	44																												
46		Build change / scope control plan	0.5 days	Thu 03/02/22	Thu 03/02/22	45																												
47		Build requirements management plan	0.5 days	Thu 03/02/22	Fri 04/02/22	46																												
48		Document impact assessment on service / support	0.5 days	Fri 04/02/22	Fri 04/02/22	47																												
49		Estimate costs to service support	0.5 days	Fri 04/02/22	Mon 07/02/2	48																												
50		Build service / support acceptance criteria	0.5 days	Mon 07/02/2	Mon 07/02/2	49																												
51		Build Project High Level Gantt Chart Plan (Summary Level)	2.25 days	Mon 07/02/2	Wed 09/02/2																													
52		Documented milestone list	0.5 days	Mon 07/02/2	Tue 08/02/22	50																												
53		Documented deliverables list	1 day	Tue 08/02/22	Wed 09/02/2	52																												
54		Documented acceptance criteria	0.5 days	Wed 09/02/2	Wed 09/02/2	53																												
55		Documented Stage 1 project mobilisation	0.25 days	Wed 09/02/2	Wed 09/02/2	54																												
56		Create Project Team Plan	5 days	Thu 10/02/22	Wed 16/02/2																													
57		Identify Project Stakeholders	0.5 days	Thu 10/02/22	Thu 10/02/22	55																												
58		Create Project Management Office Structure	1 day	Thu 10/02/22	Fri 11/02/22	57																												
59		Create Organisational Team Chart	0.5 days	Fri 11/02/22	Fri 11/02/22	58																												
60		Document Project Resource Roles & Responsibilities (RACI)	3 days	Mon 14/02/2	Wed 16/02/2	59																												
61		MILESTONE: Project Documentation Approval	0 days	Wed 16/02/2	Wed 16/02/2	27																												
62		Project Mobilisation	6 days	Thu 17/02/22	Thu 24/02/22																													
63		Obtain Project Seed Funding	1 day	Thu 17/02/22	Thu 17/02/22																													
64		Gain Approval For Project Seed Fund	1 day	Thu 17/02/22	Thu 17/02/22	60																												

Project: The Definitive Windows 11
Date: Tue 21/09/21

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Manual Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline			
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Qtr 1, 2022			Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023		
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
696		Tranche 10	38 days	Fri 17/02/23	Wed 12/04/2																						
697		Copy & Paste Required Tasks From Tranche 1 Here...	38 days	Fri 17/02/23	Wed 12/04/2	679																					
698		MILESTONE: Deployment Phase Complete	0 days	Wed 12/04/2	Wed 12/04/2	680,682,684,68																					
699																											
700		Operate	83.85 days	Fri 23/12/22	Wed 19/04/2																						
701		Project To Service Delivery Handover	83.85 days	Fri 23/12/22	Wed 19/04/2																						
702		System Readiness	3 days	Tue 27/12/22	Thu 29/12/22																						
703		Create New Platform Categories In Problem Ticket System For Windows 11	3 days	Tue 27/12/22	Thu 29/12/22	606																					
704		Create Windows 11 Catalogue For Service Requests	3 days	Tue 27/12/22	Thu 29/12/22	606																					
705		Create New Service Request Type In System For Windows 11 New Build	2 days	Tue 27/12/22	Wed 28/12/2	606																					
706		Ensure Windows 11 Flags Exist In Asset Management System	2 days	Tue 27/12/22	Wed 28/12/2	606																					
707		Ensure New Joiners Can Be Analysed For Straight Deployment To Windows 11	2 days	Tue 27/12/22	Wed 28/12/2	606																					
708		Resource Readiness	20 days	Fri 23/12/22	Thu 19/01/23																						
709		Ensure Support Staff Aware Of New System Options	3 days	Fri 23/12/22	Tue 27/12/22	484																					
710		Ensure Help Desk Team Trained In Windows 11 Problem Resolution	20 days	Fri 23/12/22	Thu 19/01/23	484																					
711		Ensure Deskside Support Team(s) Trained In Windows 11 Problem Resolution	20 days	Fri 23/12/22	Thu 19/01/23	484																					
712		Ensure PC Build Teams Trained In Win 11 Image Deployment	10 days	Fri 23/12/22	Thu 05/01/23	484																					
713		Documentation	10 days	Fri 23/12/22	Thu 05/01/23																						
714		Ensure Windows 11 Knowledgebase Exists For All Aspects Of Build & Support	10 days	Fri 23/12/22	Thu 05/01/23	484																					
715		Disaster Recovery	5 days	Wed 12/04/2	Wed 19/04/2																						
716		Ensure DR Testing Complete & Signed Off	5 days	Wed 12/04/2	Wed 19/04/2	698																					
717		Continuous Improvement	70.85 days	Fri 23/12/22	Fri 31/03/23																						
718		Track Windows 11 Problem Ticket Volumes	30 days	Fri 17/02/23	Fri 31/03/23	679																					
719		Analyse Ticket Volumes For Top 10 End User Issues	7 days	Fri 30/12/22	Mon 09/01/2	703																					
720		Feedback To Engineering Build Roadmap	3 days	Tue 10/01/23	Thu 12/01/23	719																					
721		Ensure Process In Place To Update Core Image & Existing Windows 11 Machines	5 days	Fri 23/12/22	Thu 29/12/22	484																					
722		MILESTONE: Operate Phase Complete	0 days	Wed 19/04/2	Wed 19/04/2	701,717																					
723																											
724		Project Closedown	10 days	Wed 19/04/2	Wed 03/05/2																						
725		Identify Outstanding Items To Complete (Migrations In BAU etc)	5 days	Wed 19/04/2	Wed 26/04/2	722																					
726		Produce High Level Budget vs Actuals Report	2 days	Wed 19/04/2	Fri 21/04/23	722																					
727		Produce Resource Forecast vs Actuals Spreadsheet	2 days	Wed 19/04/2	Fri 21/04/23	722																					
728		Produce Timeline Forecast vs Spreadsheet	2 days	Wed 19/04/2	Fri 21/04/23	722																					
729		Produce Detailed Budget vs Actuals Spreadsheet	2 days	Fri 21/04/23	Tue 25/04/23	726																					
730		Produce High Level Statistics Report (Migrations, Apps etc)	3 days	Wed 19/04/2	Mon 24/04/2	722																					
731		Produce Lessons Learnt Document	10 days	Wed 19/04/2	Wed 03/05/2	722																					
732		Present Project Closedown Report To Senior Stakeholders	1 day	Wed 19/04/2	Thu 20/04/23	722																					
733		MILESTONE: Project Closedown Complete	0 days	Wed 03/05/2	Wed 03/05/2	724																					

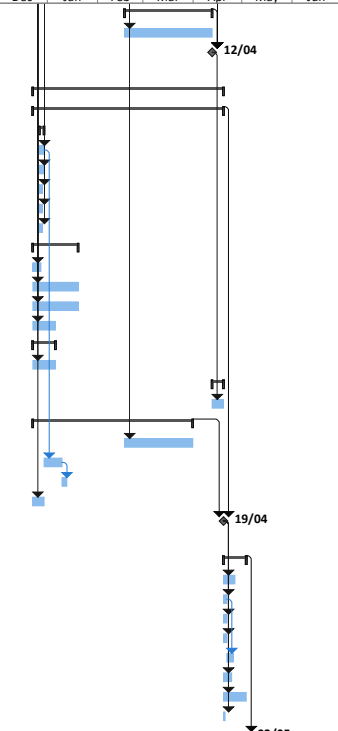

Project: The Definitive Windows 1
Date: Tue 21/09/21

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Manual Progress
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline	Manual Progress
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress	Manual Progress
